


ID	Unique ID	% Complete	Task Name	3Q09				4Q09			1Q10			2Q10	
				Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May
1	466	50%	Middleware/Infrastructure Management, Coordination												
2	194	50%	DC3 coordination												
3	467	50%	Infrastructure maintenance												
4	427	15%	Middleware	[Solid black bar]											
5	621	100%	DC3b Start Date				8/3								
6	705	0%	Two-Month Milestone						10/1						
7	1	30%	SW Quality Assurance	[Solid black bar]											
8	9	30%	Acquire SQA support tools	[Solid black bar]											
9	10	10%	Configurable tool to perform Lsst software standards checking	[Solid black bar]											
10	480	15%	Benchmark	[Solid black bar]											
11	482	30%	C++												
12	481	0%	Python												
13	478	0%	Acquire												
14	11	90%	coverage analysis tool												
15	488	90%	Release for developer use												
16	37	28%	Build System	[Solid black bar]											
17	68	34%	VMs	[Solid black bar]											
18	569	10%	Maintain automated testing structure												
19	41	75%	(BB) support distributable VMs for new develop												
20	72	48%	deploy automated, multi-platform testing system												
21	69	62%	install and configure initial testing system												
22	74	5%	configure test system for automated V&V												
23	44	7%	implement Software Quality Assurance procedures relevant to build process												
24	45	10%	within Ticket branch development												
25	46	10%	build warnings if coding standards check fails												
26	47	10%	build warnings if unittest doesn't satisfy DC3 coverage requirement												
27	51	10%	Nightly build of development trunk												
28	52	10%	any failures cause automatic 'Failed Nightly Build' ticket at high priority												
29	53	0%	Production Release sanity check												
30	54	0%	any failure causes automatic 'Failed Production sanity check' ticket at high priority												
31	55	0%	auxiliary automatic notification to highest authority on failure (separate from ticket)												
32	56	0%	Configuration Management: 'Build' upgrade												
33	57	0%	Standards: specify requirement to version and archive build's provenance;												
34	58	0%	Configuration Management: define procedure to satisfy that requirement;												
35	59	0%	Configuration Management: implement its installation												
36	622	0%	EUPS Revisions												

Laher Russ
Allsma

Baker Bill[10%]
Baker Bill[5%]

Project: LSST-DC3-v1.8-updated-07.2
Date: Tue 9/8/09


Task Progress Summary External Tasks Deadline
Split Milestone Project Summary External Milestone

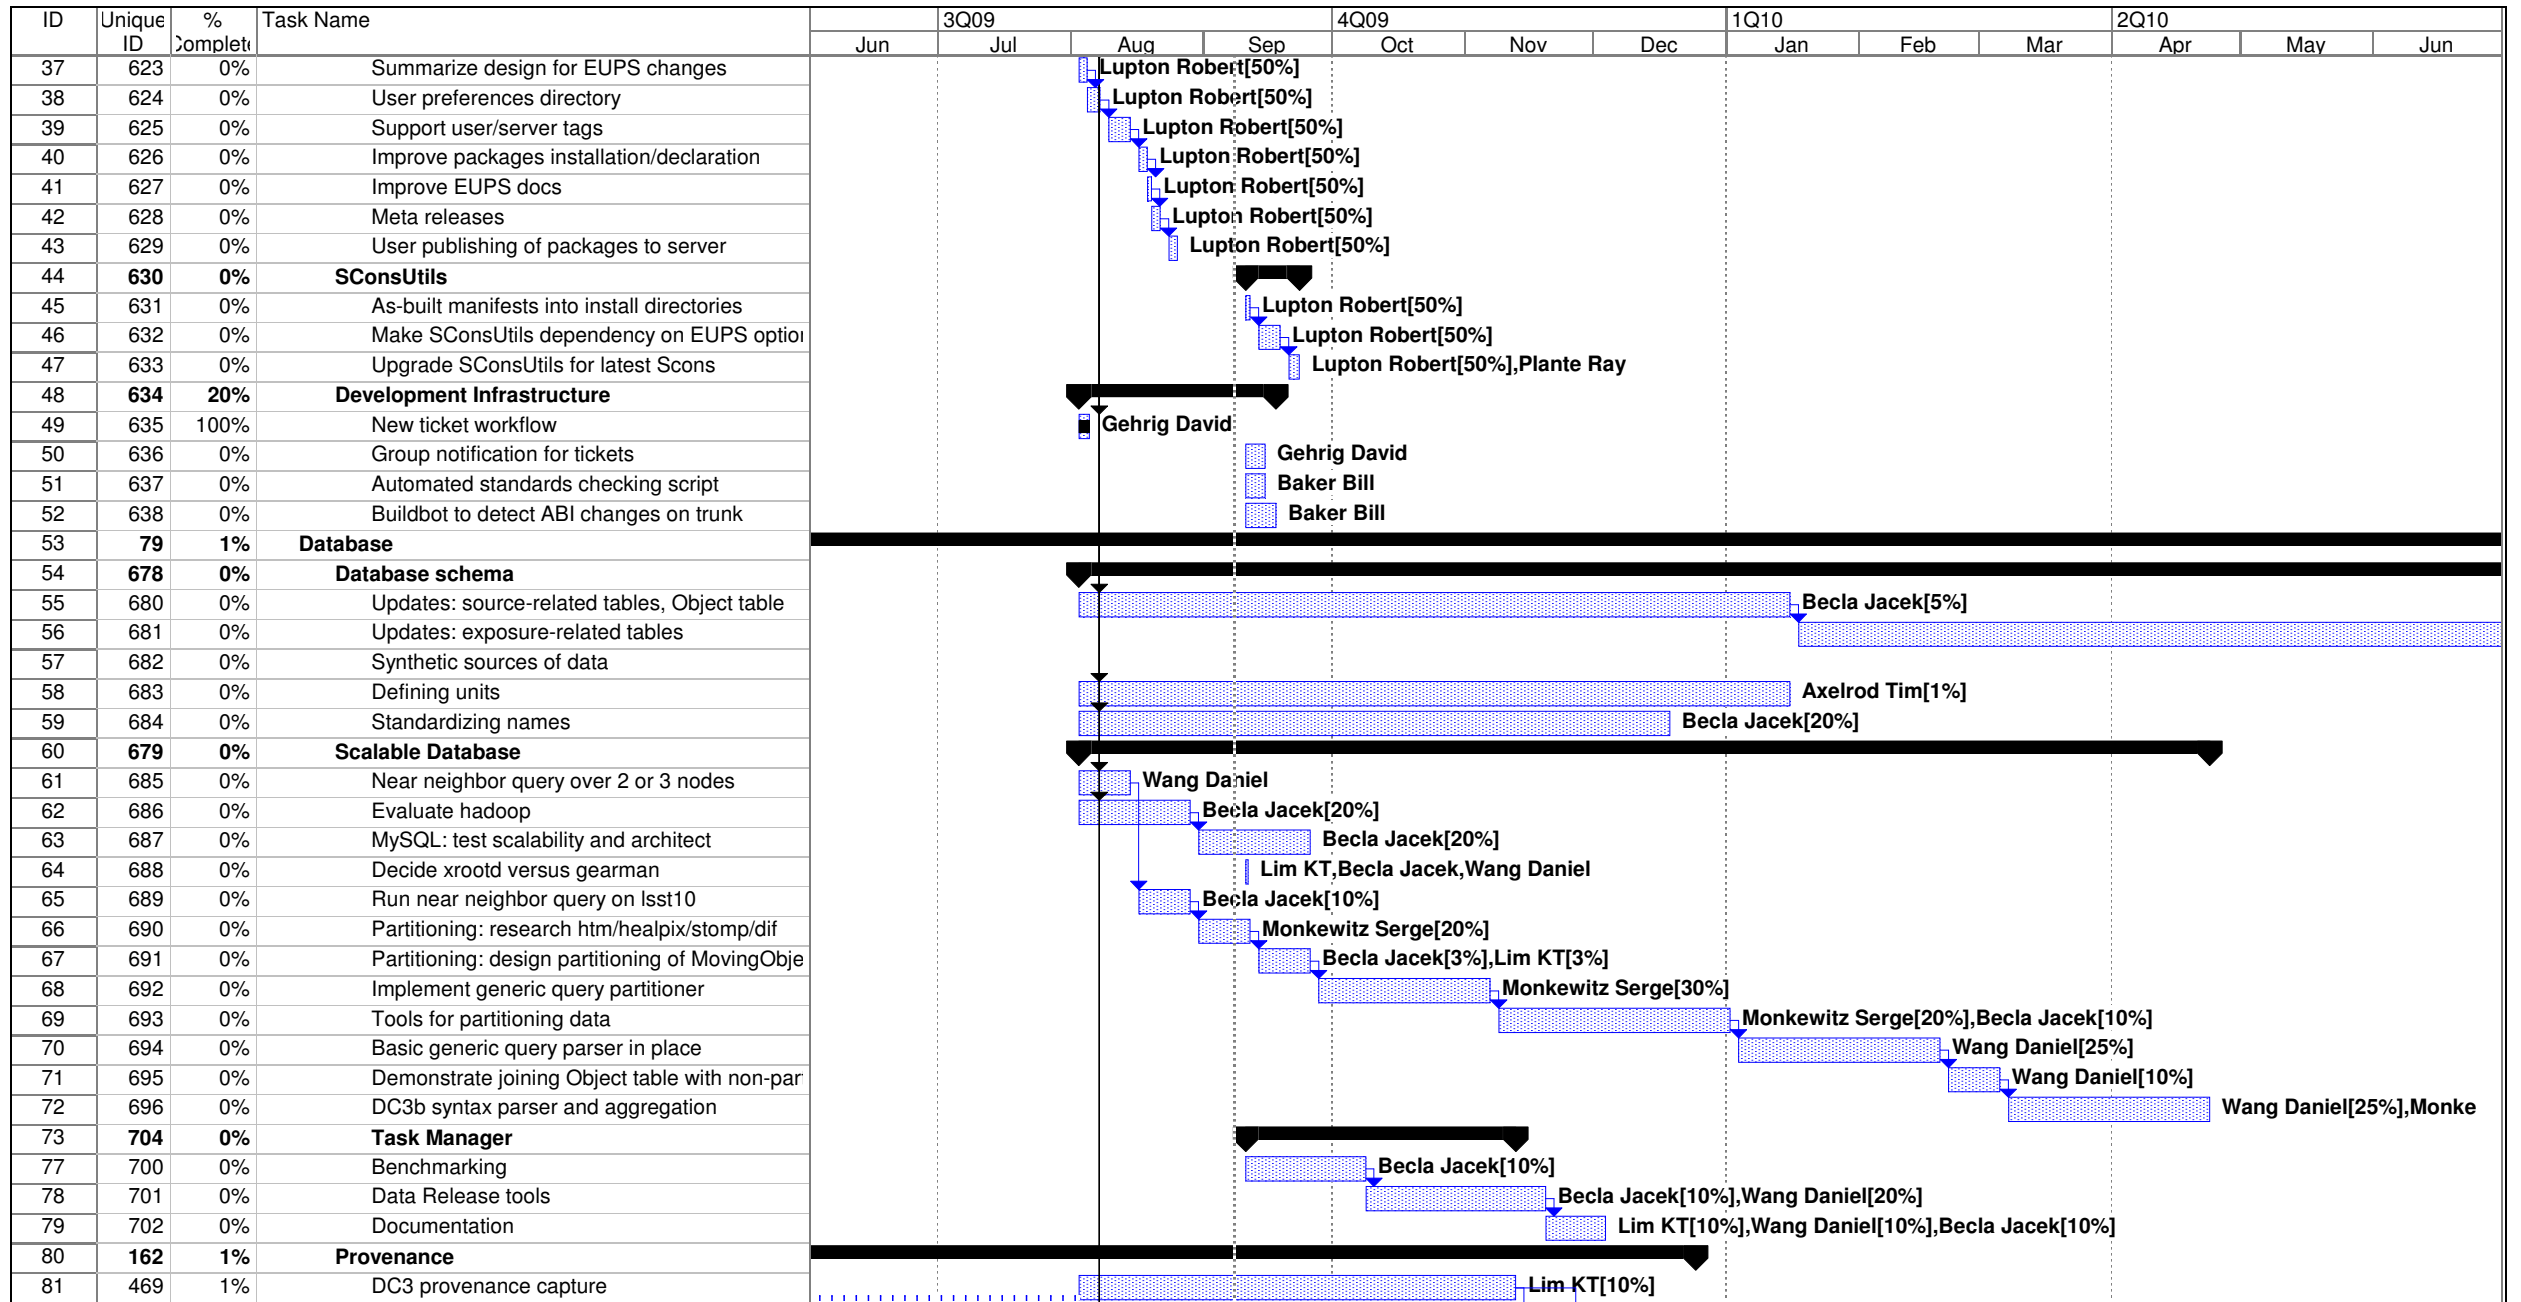

Project: LSST-DC3-v1.8-updated-07.2
Date: Tue 9/8/09


Task: Progress Summary External Tasks Deadline

Split: Milestone Project Summary External Milestone

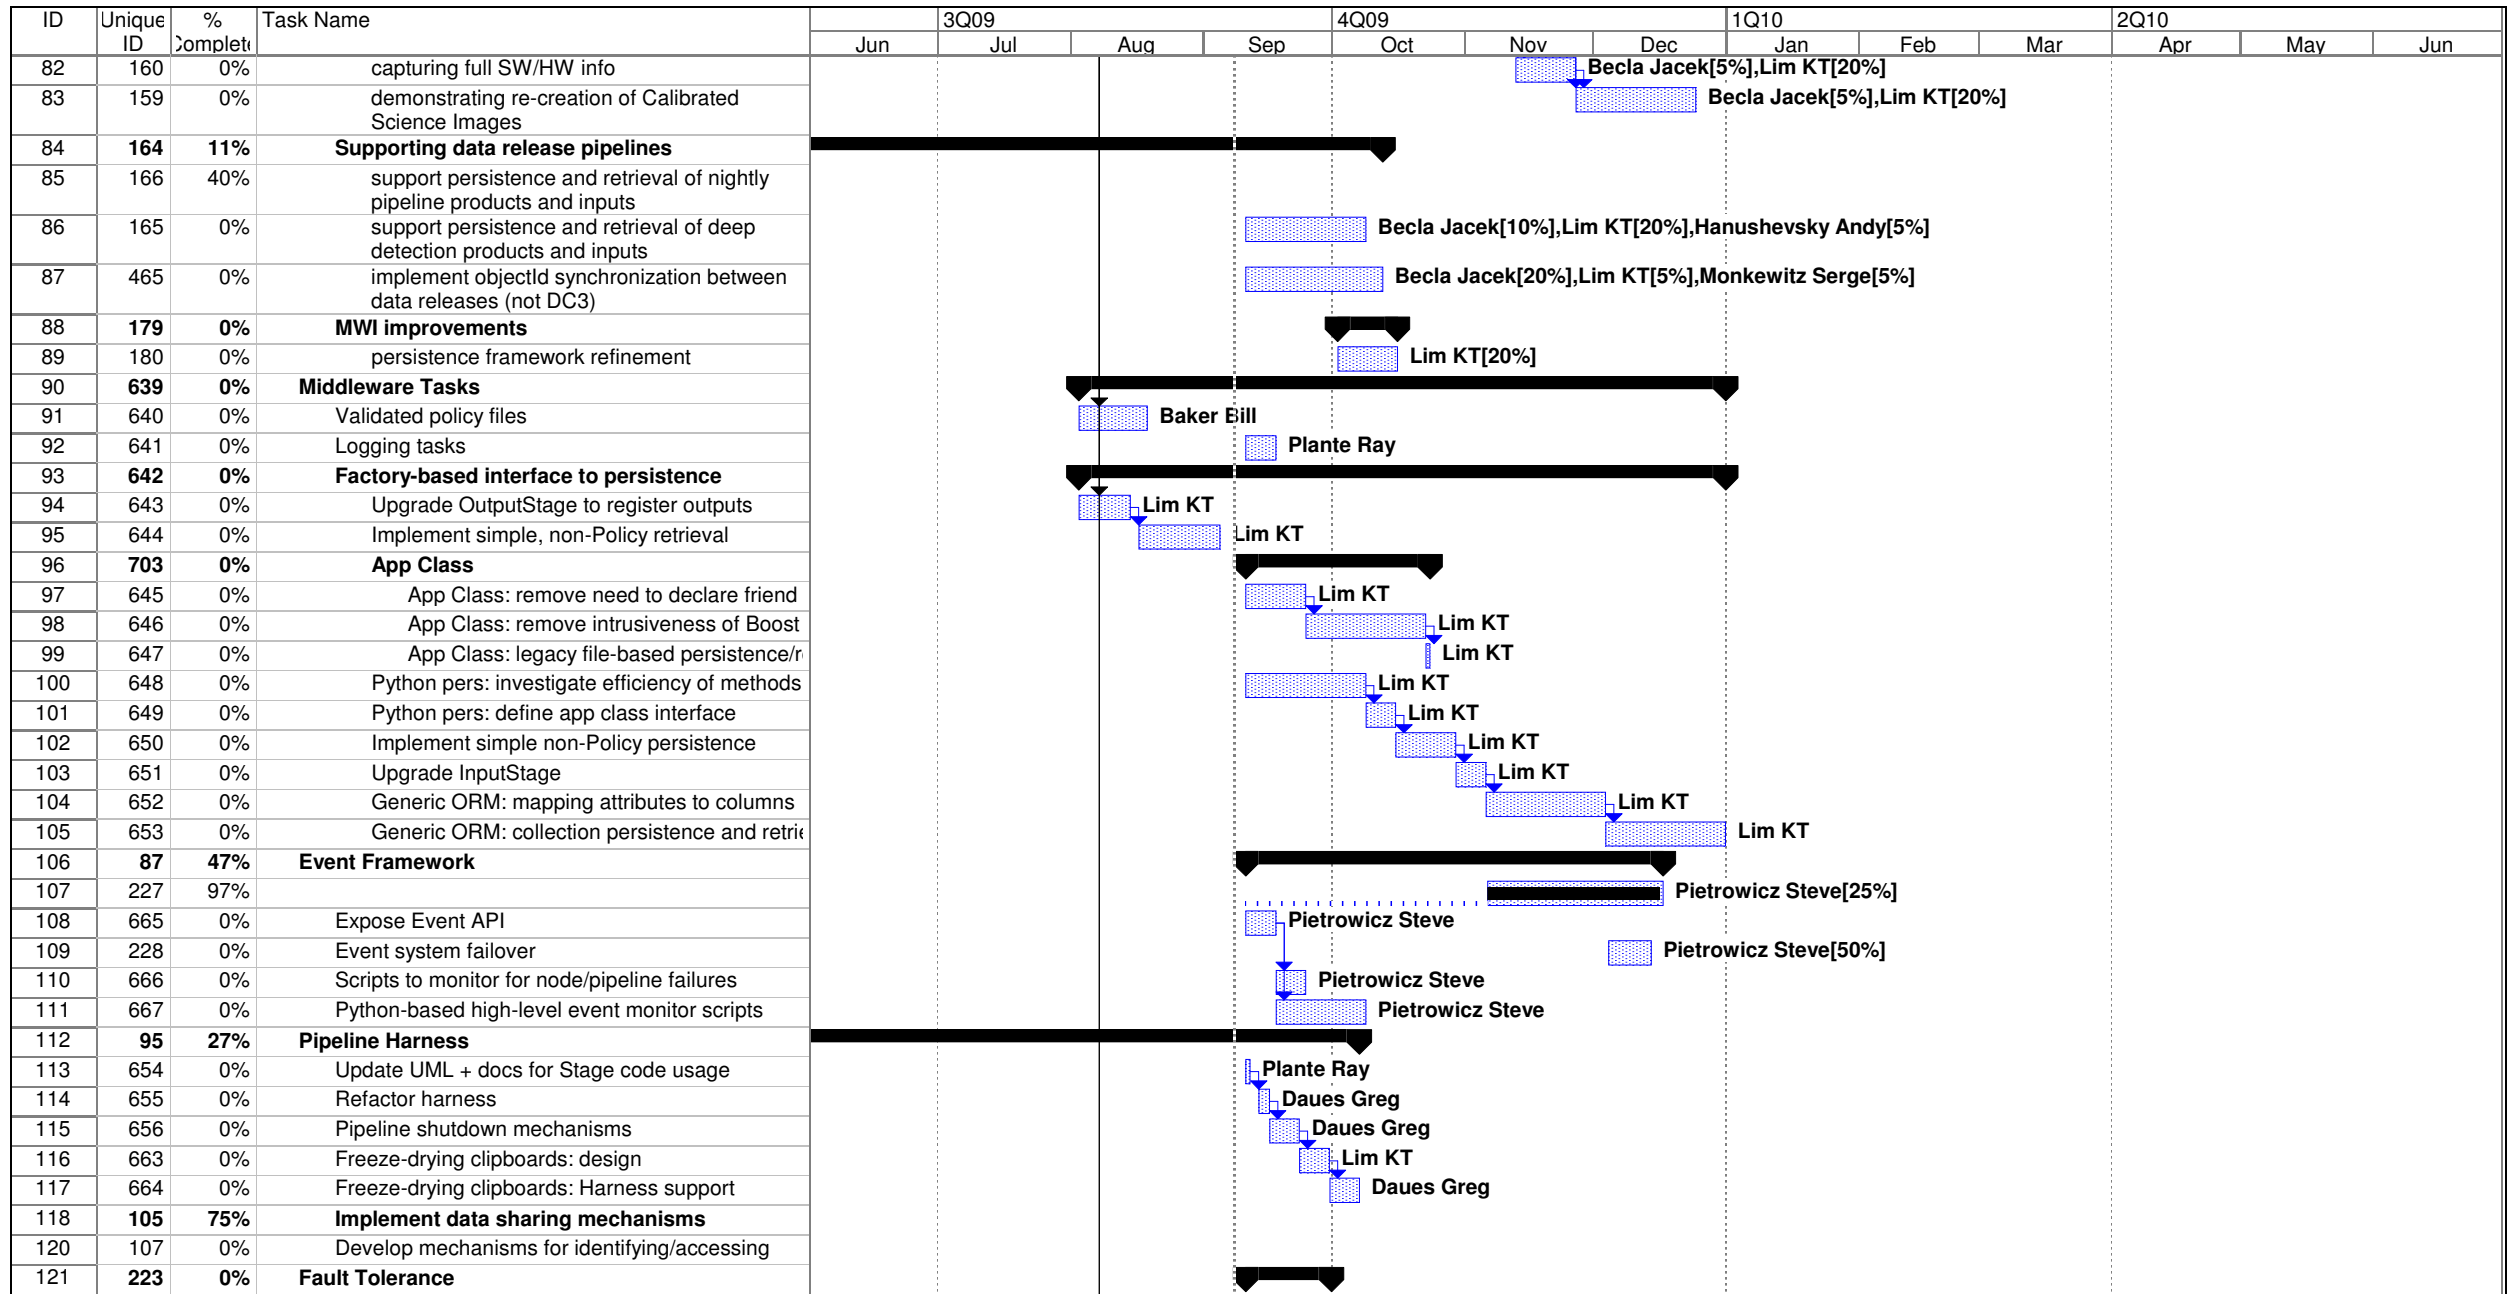

Project: LSST-DC3-v1.8-updated-07.2
Date: Tue 9/8/09

Task Progress Summary External Tasks Deadline
 Split Milestone Project Summary External Milestone

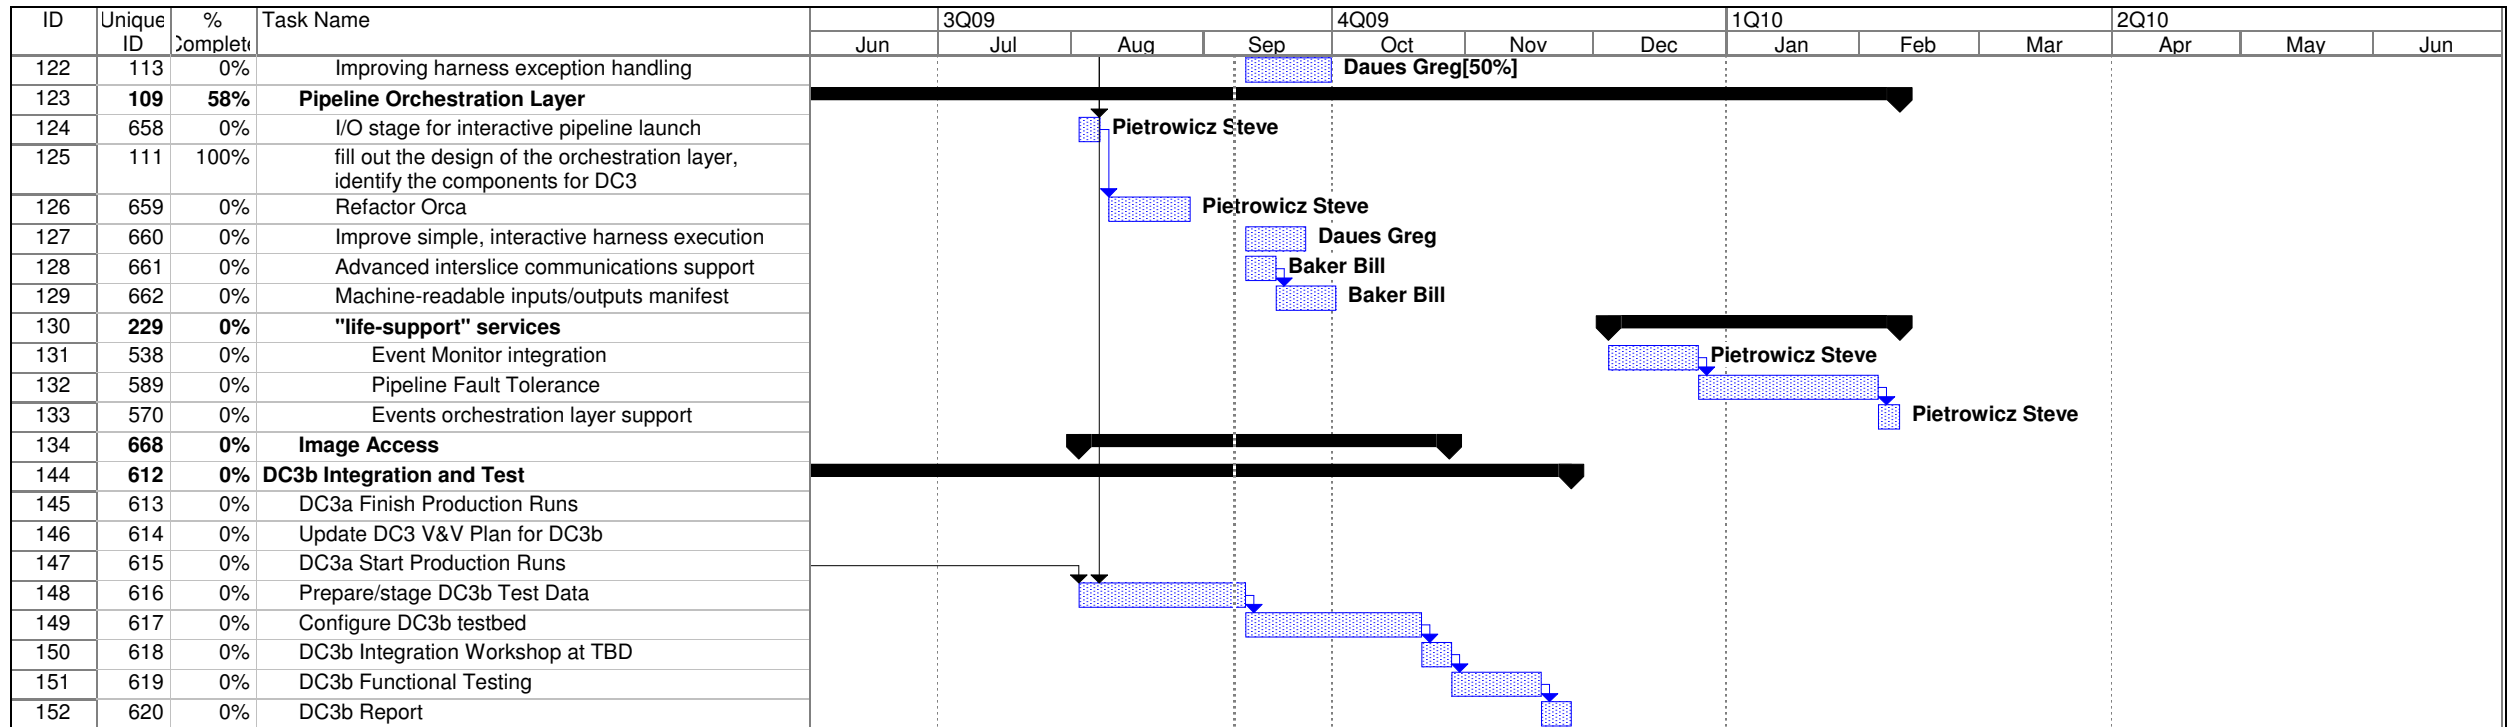

Project: LSST-DC3-v1.8-updated-07.2
Date: Tue 9/8/09

